

# 2019 Bituminous Street Improvements St. Joseph, Minnesota



STJOE 147693

# Project Update

## Project Contacts

### General Contractor

Knife River Corp.

Project Manager

Andy Hicks

[andy.hicks@kniferiver.com](mailto:andy.hicks@kniferiver.com)

763-286-0678

Project Superintendent

Todd Puhalla

320.248-1508

### Subcontractors

#### Sewer & Water Main

C&L Excavating

Kevin Cox

320.363.1221

#### Traffic Control

All State

Manny Kissner

320.685.9911

#### Concrete Flatwork

West Star Curb

Dean

320.764.9582

#### Turf Establishment

North Star Landscaping

Sean Grefe

320.597.2500

#### Grading

Craig Bardson Excavating

Ben Bardson

320.845.4952

### City Engineer

Randy Sabart, PE

320.229.4348

[rsabart@sehinc.com](mailto:rsabart@sehinc.com)

### SEH Construction Observer

Jerry Siegfried

320.980.4107

[jsiegfried@sehinc.com](mailto:jsiegfried@sehinc.com)

November 2019 | Project Update No. 2

## Thank You!

The project team would like to thank you for your cooperation on the project to date. Your continued patience and understanding makes difficult construction move ahead much more smoothly. For those of you who have contacted SEH with questions about the project, we will continue to make every attempt to provide answers to you in a timely manner. We encourage you to call or email with questions.

For any questions, Jerry Siegfried and Shawn Kapsch, SEH's Project Representatives, will be on-site during construction to observe project progress and the Contractor's work. Jerry and Shawn are the fastest link to problem solving because they communicate directly with everyone on the construction team. Do not hesitate to contact Jerry or Shawn with any questions you may have. If you are unable to reach Jerry or Shawn in the field, please contact Bill Zidon at the SEH Office at 320.229.4309.

## Schedule Update

The first layer of bituminous has been completed on Old Highway 52, Cypress Drive, Elm Street, Baker Street, Callaway Street, 12<sup>th</sup> Avenue SE, Pondview Lane E, and 13<sup>th</sup> Avenue SE and all concrete flatwork has been completed on the project. Paving, aggregate shouldering, and striping have been completed on Jade Road.

Due to the prevailing poor weather conditions and a desire to ensure a high quality of workmanship, the Contractor will complete the remaining work in the 2020 construction season. This work consists of the following:

- Resurfacing portions of 4<sup>th</sup> Avenue SE, Western Court, 12<sup>th</sup> Avenue SE, Pond View Lane, Callaway Street, Cary Court, Cedar Court, Dale Street, Birch Street W, Ash Street W, and 1<sup>st</sup> Avenue NW.
- Mill and pave 4<sup>th</sup> Avenue NE.
- The final layer of bituminous will be paved on Old Highway 52, Cypress Drive, Elm Street, Baker Street, Callaway Street, 12<sup>th</sup> Avenue SE, Pondview Lane E, and 13<sup>th</sup> Avenue SE.
- Finalizing turf establishment on all disturbed areas.

We will issue another newsletter when the Contractor plans to resume construction activities in the 2020 construction season. The final completion date for the project is July 10, 2020.


## Description of Remaining Work

The street resurfacing portion of the project consists of edge milling the outside 6 feet of the existing pavement about 1-inch deep and constructing a new 1.5-inch thick layer of bituminous pavement on 1<sup>st</sup> Avenue NW, W Birch Street, W Ash Street, 4<sup>th</sup> Avenue SE, Western Court, 12<sup>th</sup> Avenue SE, Callaway Street, Pondview Lane, Cary Court, Cedar Court, and Dale Street. There will also be some spot pavement reconstruction areas.

4<sup>th</sup> Avenue NE will be resurfaced by removing (milling) the full thickness of the existing pavement surface and paving two new layers of bituminous pavement on the existing aggregate base.

# Construction Site Safety

There will be some deep utility trench construction and, of course, heavy machinery operating on the construction site. Heavy equipment and construction in progress can be strong attractions to everyone, especially children. Warn your children not to play near machinery and construction material storage areas. Your help in keeping children and other bystanders away from the construction area will ensure that the project will progress smoothly!

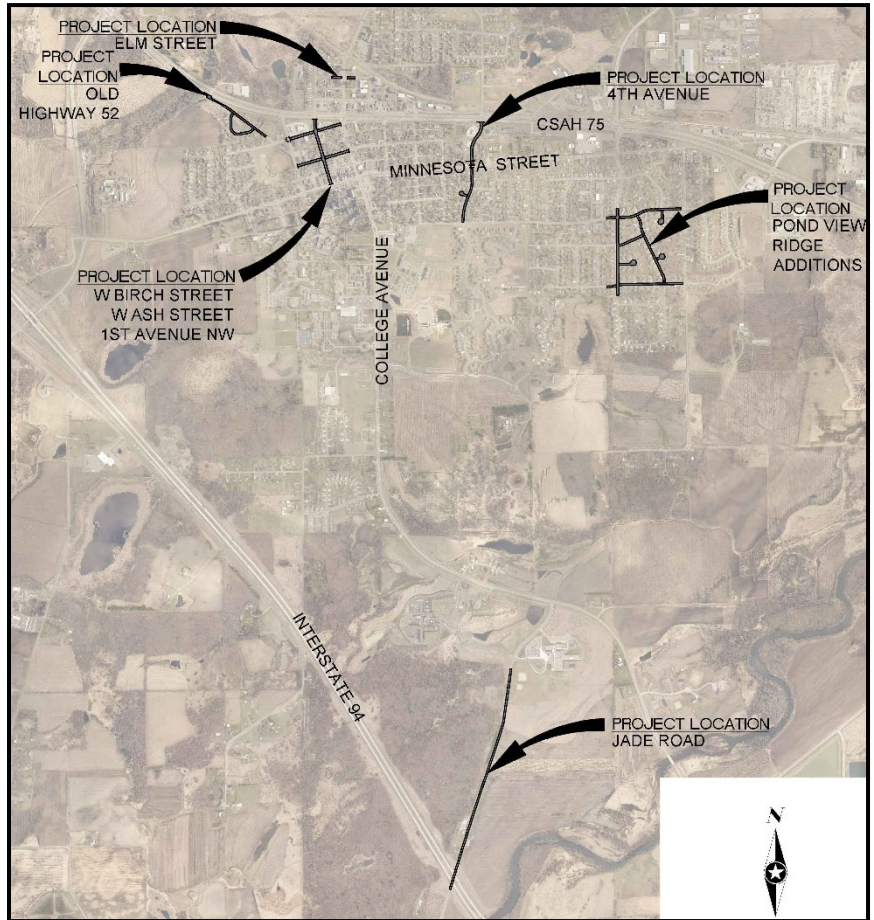

Short Elliott Hendrickson Inc.  
1200 25th Avenue South  
P.O. Box 1717  
St. Cloud, MN 56302-1717



# Project Update

2019 Bituminous Street Improvements  
St. Joseph, Minnesota
